

# SEMSWA CIP Project Status Update

January, 2011

## PROJECT: Piney Cr. Stabilization (Tower to Liverpool)

**DESCRIPTION:** Design and construction of stream stabilization of Piney Creek. UDFCD joint project.

**BUDGET:** \$550,000

**STATUS:** Construction underway

**CHANGE SINCE LAST REPORT:** CONSTRUCTION STARTED.

### **MILESTONES:**

- Construction Completion:



## PROJECT: Cottonwood Creek (Easter to Briarwood)

**DESCRIPTION:** Design and construction of stream stabilization

**BUDGET:** \$1,391,677

**STATUS:** Construction completed

**CHANGE SINCE LAST REPORT:** Construction completed

### MILESTONES:

- Project Acceptance:



## PROJECT: Forest Park Stabilization

**DESCRIPTION:** Design and construction of stream stabilization of Big Dry Creek Tributary B


**BUDGET:** \$225,000

**STATUS:** Final design in for review; Section 404 Permit acquired.

**CHANGE SINCE LAST REPORT:** REVIEW OF FINAL DESIGN COMPLETED

### MILESTONES:

- Design Completion: Winter 2011
- Construction Start: Fall 2011

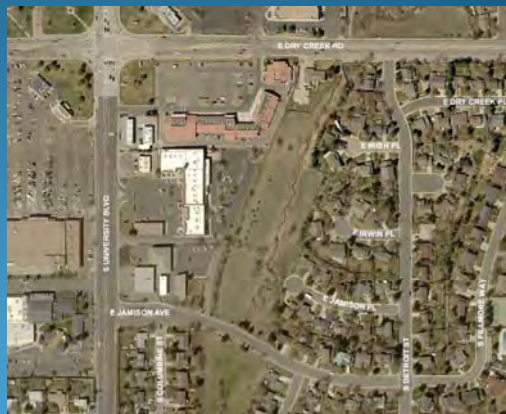

## PROJECT: Little Dry Creek Reach 6

**DESCRIPTION:** Design of stream stabilization of Little Dry Creek. UDFCD joint project.

**BUDGET:** \$128,845

**STATUS:** Final design in for review; Section 404 Permit submitted.

**CHANGE SINCE LAST REPORT:**  
NONE

### MILESTONES:

- Design Completion: 2011
- Construction Start: 2013



## PROJECT: Lone Tree Creek Pond L-2

**DESCRIPTION:** Design and construction of Phase 1 of the regional stormwater pond

**BUDGET:** \$250,000

**STATUS:** Final design complete; Section 404 Permit acquired.

**CHANGE SINCE LAST REPORT:**  
EASEMENT ACQUISITION COMPLETED

### MILESTONES:

- Construction Start: Fall 2011



## PROJECT: West Toll Gate Creek at Foxhill Park

**DESCRIPTION:** Design and construction of stream stabilization improvements


**BUDGET:** \$350,000

**STATUS:** CONSTRUCTION UNDERWAY

**CHANGE SINCE LAST REPORT:** CONSTRUCTION STARTED

**MILESTONES:**

- Construction Completion: April 2011

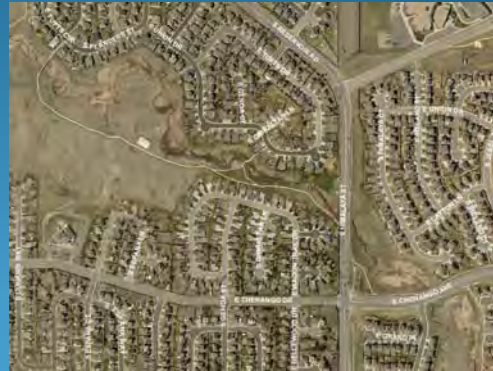

## PROJECT: Cherry Creek Stabilization at Eco Park

**DESCRIPTION:** Design and construction of stream stabilization. UDFCD joint project.

**BUDGET:** \$3,450,000

**STATUS:** Preliminary design complete

**CHANGE SINCE LAST REPORT:** PRELIMINARY DESIGN COMPLETION

**MILESTONES:**

- Design Completion: Summer 2011
- Construction Start: Fall 2011



## PROJECT: Lone Tree Creek Pond L-1 West

**DESCRIPTION:** Design and construction of the regional stormwater pond.

**BUDGET:** \$225,000

**STATUS:** Final design complete; Section 404 Permit acquired.

**CHANGE SINCE LAST REPORT:** CONSTRUCTION BIDS RECEIVED (12/17/11)

### MILESTONES:

- Construction Start: February 2011



## PROJECT: Goldsmith Gulch Culvert at Caley Ave

**DESCRIPTION:** Design and construction of culvert replacement. UDFCD joint project.

**BUDGET:** \$200,000

**STATUS:** Preliminary design completed.

**CHANGE SINCE LAST REPORT:** PRELIMINARY DESIGN REVIEW COMPLETED.

### MILESTONES:

- Design Completion: May 2011
- Construction Start: June 2011



## PROJECT: Heritage Place Lateral 2

DESCRIPTION: Storm sewer

BUDGET: \$160,000

STATUS: Construction complete

CHANGE SINCE LAST REPORT:  
AS-BUILT DRAWINGS SUBMITTED

MILESTONES:

- Project Acceptance:



## PROJECT: Windmill Creek Pond W-1

DESCRIPTION: Design and construction of Phase 1 of the regional stormwater pond.

BUDGET: \$300,000

STATUS: Final design underway

CHANGE SINCE LAST REPORT:  
PRELIMINARY PLAN REVIEW COMPLETED

MILESTONES:

- Design Completion: Summer 2011
- Construction Start: Fall 2011



## PROJECT: E. Toll Gate Creek Pond @ Gun Club Rd

DESCRIPTION: Design and construction of Phase 1 of the regional stormwater pond


BUDGET: \$190,000

STATUS: DESIGN PROPOSALS RECEIVED (1/18/11); SELECTION IN FEB. 2011

CHANGE SINCE LAST REPORT: DESIGN PROPOSALS RECEIVED

### MILESTONES:

Design Start: March 2011

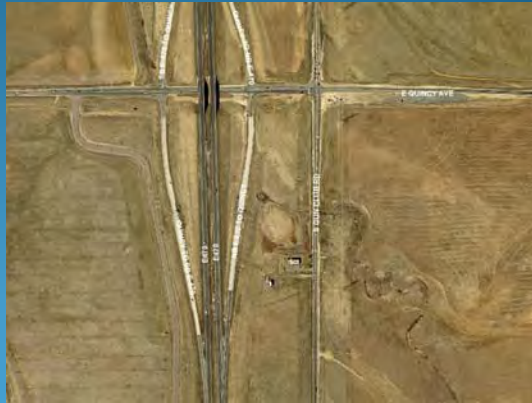

## PROJECT: Drop Structure on Piney Creek @ Parker Rd

DESCRIPTION: Design and construction of drop structure to replace failed structure

BUDGET: \$190,000

STATUS: DESIGN ON HOLD PENDING COMPLETION OF PINEY CREEK MASTER PLAN

CHANGE SINCE LAST REPORT: NONE

### MILESTONES:

Design Start: 2012



## PROJECT: Cherrybrook Detention Pond

**DESCRIPTION:** Design and construction of subregional stormwater pond

**BUDGET:** \$340,000

**STATUS:** DESIGN ON HOLD  
PENDING COMPLETION OF  
PINEY CREEK MASTER PLAN

**CHANGE SINCE LAST REPORT:**  
NONE

**MILESTONES:**

- Design Start: 2012



## PROJECT: Cherry Creek: Arapahoe Rd to State Park

**DESCRIPTION:** Design of the regional stream improvements. UDFCD joint project.

**BUDGET:** \$ 200,000

**STATUS:** Request For Proposals (RFP) being prepared

**CHANGE SINCE LAST REPORT:**  
DRAFT RFP COMPLETED

**MILESTONES:**

- Design Start: April 2011



## PROJECT: Willow Creek (Quebec St to Dry Creek Rd)

**DESCRIPTION:** Design and construction of stream improvements. UDFCD joint project.

**BUDGET:** \$400,000

**STATUS:** Design underway

**CHANGE SINCE LAST REPORT:**  
DESIGN STARTED

### MILESTONES:

- Design Completion: Fall 2011
- Construction Start: Winter 2011

