


SEMSWA CIP Project Status Update

February, 2012

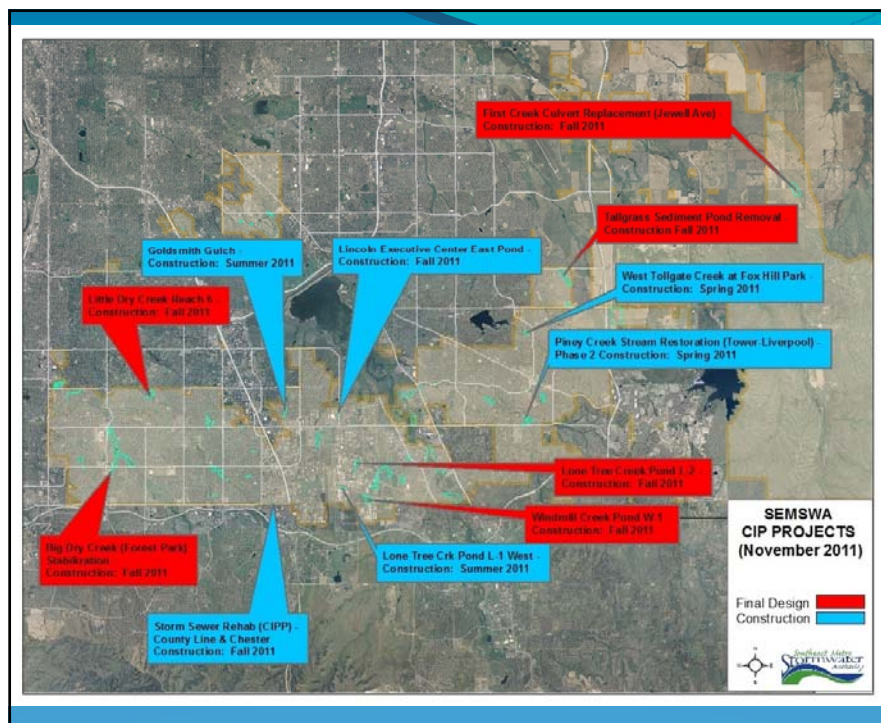

PROJECT: DOVE CREEK REGIONAL POND D-2

DESCRIPTION:

CONSTRUCTION OF REGIONAL
DETENTION -WATER QUALITY
POND

BUDGET: \$803,380

STATUS: CONSTRUCTION
STARTED

CHANGE SINCE LAST REPORT:
Construction Started

MILESTONES:

Construction Complete:
June, 2012



PROJECT: WINDMILL CREEK REGIONAL POND W-1

DESCRIPTION:

CONSTRUCTION OF REGIONAL
DETENTION -WATER QUALITY
POND

BUDGET: \$916,715

STATUS: CONSTRUCTION
STARTED

CHANGE SINCE LAST REPORT:
Construction Started

MILESTONES:

Construction Complete:
June, 2012



PROJECT: LONE TREE CREEK REGIONAL POND L-2

DESCRIPTION:

CONSTRUCTION OF REGIONAL
DETENTION POND

BUDGET: \$686,483

STATUS: CONSTRUCTION
STARTED

CHANGE SINCE LAST REPORT:

Construction Started

MILESTONES:

Construction Complete:
July, 2012



PROJECT: LINCOLN EXECUTIVE CENTER EAST POND

DESCRIPTION:

CONSTRUCTION OF SUB-
REGIONAL DETENTION
& WATER QUALITY POND

BUDGET: \$366,530

STATUS: CONSTRUCTION IN
PROGRESS

CHANGE SINCE LAST REPORT:

Construction Started

MILESTONES:

Construction Complete:
March, 2012



PROJECT: BIG DRY CREEK TRIBUTARY B – CHANNEL IMPROVEMENTS

DESCRIPTION:

CONSTRUCTION OF 950'
CHANNEL IMPROVEMENTS

BUDGET: \$267,330

STATUS: CONSTRUCTION IN
PROGRESS

CHANGE SINCE LAST REPORT:

Construction Started

MILESTONES:

Construction Complete:
May, 2012



FALL - WINTER 2011/2012 CONSTRUCTION PROJECTS

<u>PROJECT</u>	<u>ESTIMATED COST (\$)</u>	<u>ESTIMATED COST for PROJECTS BID (\$)</u>	<u>LOW BID (\$)</u>
JEWELL AVENUE CULVERT REPLACEMENT	320,000		
LINCOLN EXECUTIVE CENTER EAST POND	390,000	390,000	366,530
WINDMILL CREEK POND W-1 (PHASE 1)	850,000	850,000	763,764
FOREST PARK - TRIBUTARY B STABILIZATION	280,000	280,000	232,461
LONE TREE CREEK POND L-2 (PHASE 1)	700,000	700,000	588,712
TALLGRASS SEDIMENT POND REMOVAL	285,000		
DOVE CREEK POND D-2	750,000	750,000	647,073
TOTAL	3,575,000	2,970,000	2,598,540
